



JUNE 2026 BOND OVERSIGHT COMMITTEE MEETING



AGENDA

- Welcome and introductions
- 2024 Bond Projects – General information
- 2024 Bond Projects – project-by-project update
- Committee business
- What's ahead
- Wrap Up
- Adjourn

WELCOME

- Opening remarks
- Introductions
- What are you hearing about the bond projects?

2024 Bond Projects

General Information

2024 Bond Projects: Financial Overview

2024 Bond Projects - Schedules and Cash Flow										
Bond Sales		\$175m			\$150m		\$275m	\$132m		\$732m
Projects	Budget	2024/2025	2025/2026	2026/2027	2027/2028	2028/2029	2029/2030	2030/2031	2031/2032	Totals
BLHS Classroom Addition & Intersection	\$76.9m	\$2.0m	\$6.0m	\$40.0m	\$28.9m					\$76.9m
Sumner HS Phase 2 West Building	\$114.0m	\$2.0m	\$6.0m	\$40.0m	\$40.0m	\$26.0m				\$114.0m
New Middle School at Tehaleh	\$200.0m	\$2.0m	\$6.0m	\$20.0m	\$88.0m	\$84.0m				\$200.0m
Liberty Ridge Elementary Improvements	\$2.9m		\$0.8m	\$1.4m	\$0.6m					\$2.9m
Crestwood Elementary Improvements	\$2.9m		\$0.8m	\$1.4m	\$0.6m					\$2.9m
Tehaleh Heights Elementary Expansion	\$19.0m		\$1.0m	\$3.0m	\$15.0m					\$19.0m
Donald Eismann Ele. Queueing, Parking & Field	\$7.8m		\$1.0m	\$6.8m						\$7.8m
Daffodil Valley Ele. Field Improvements	\$6.0m			\$6.0m						\$6.0m
Sumner HS (Master Plan Build Out)	\$298.2m				\$2.0m	\$54.0m	\$116.2m	\$92.0m	\$34.0m	\$298.2m
Energy Efficiency Improvements*	\$4.0m	\$0.3m	\$0.8m	\$1.0m	\$0.5m	\$1.0m	\$0.5m			\$4.0m
Totals		\$6.3m	\$22.4m	\$119.7m	\$175.7m	\$165.0m	\$116.8m	\$92.0m	\$34.0m	\$731.8m
Ending Balance		\$168.8m	\$146.4m	\$26.7m	\$1.0m	\$111.0m	\$126.2m	\$34.2m	\$0.2m	
Actual Totals		\$4.8m	\$9.8m							
Actual Ending Balance		\$172.9m	\$167.6m							

Green = Planning/Permitting

Blue = Construction

Light Blue = Schedule Reduction

Purple = Schedule Delay

* Energy Improvements are an ongoing process


Note: Dollar amounts are in millions

To 4/26

Expenditures do not include costs of selling bond or general overhead, including BOC

2024 Bond Projects: What is SEPA?

State Environmental Policy Act

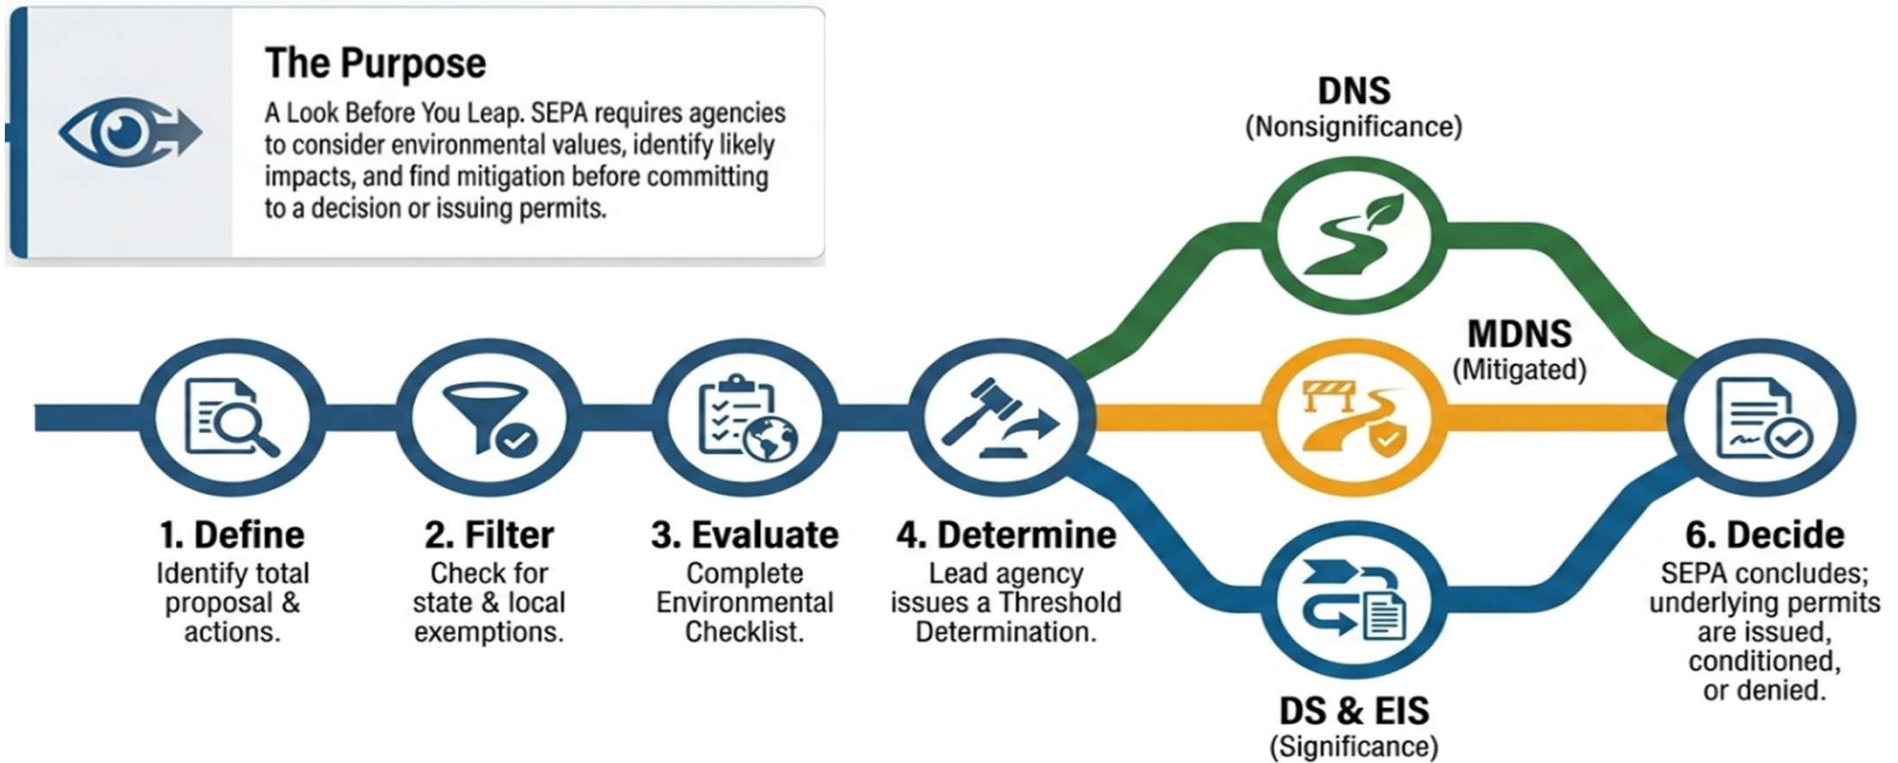

2024 BOND PROJECT UPDATES

Bonney Lake HS Expansion - Project Team

Architect: BCRA, Inc.

GC/CM Contractor: Korsmo Construction

Structural Engineer: PCS Structural Solutions

Mechanical/Electrical Engineer: GFT

Civil Engineer: Sitts & Hill Engineers

Landscape Architect: Fora Landscape Architects

Bonney Lake HS Expansion - Project Updates

- Permit received for 500 Wing Piping Replacement
- Scheduled to start demo, wall construction and 500 wing piping in the summer
- Construction sequencing, paths of travel, safety and communication agreed by all parties
- SEPA submitted. Comment period ended June 1st.

Bonney Lake HS Expansion - Risks and Opportunities

Risks:


- Permit status - Responded to initial comments May 27
- Construction bid environment
- Gas prices' effect on material costs
- County traffic impact analysis comments

Opportunities:



- Joint outreach event held in May. Another scheduled for July.




Ground floor

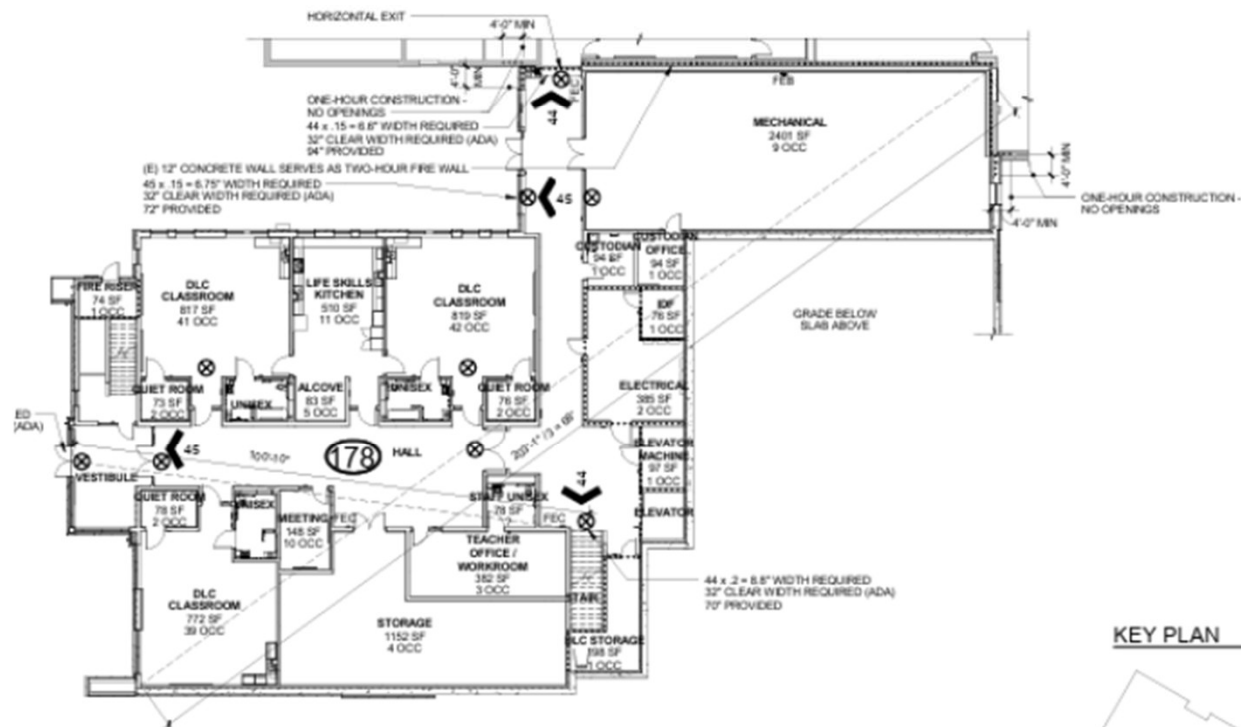


First floor

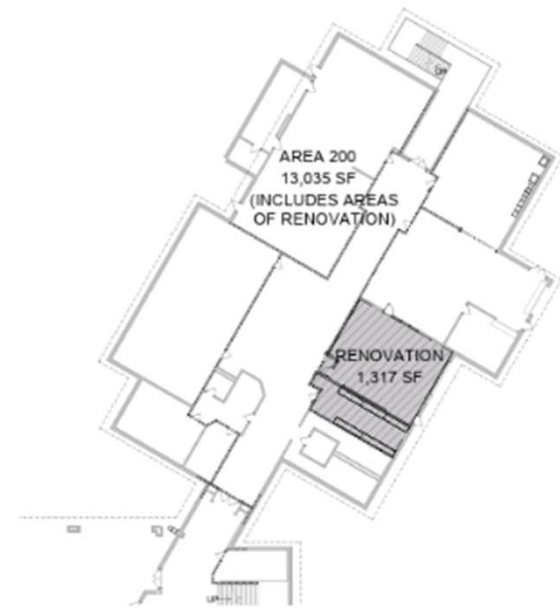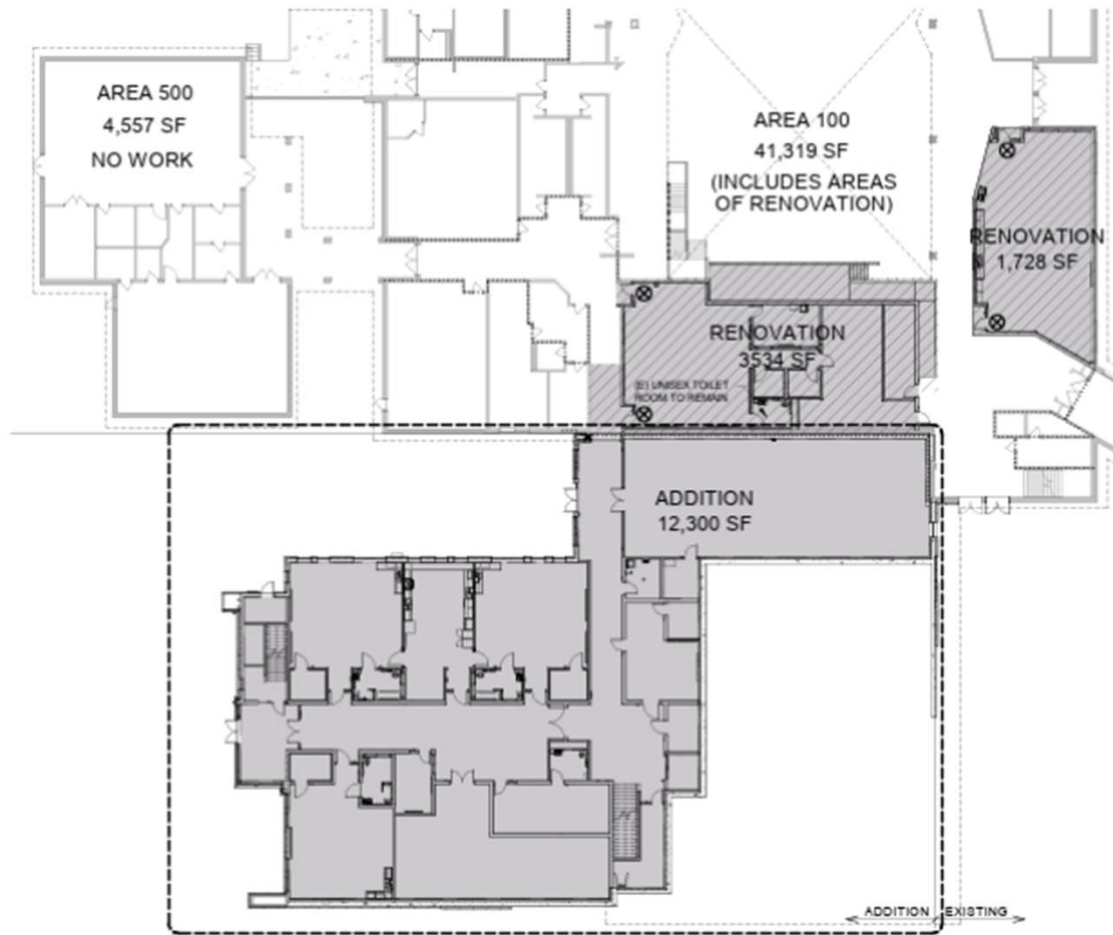

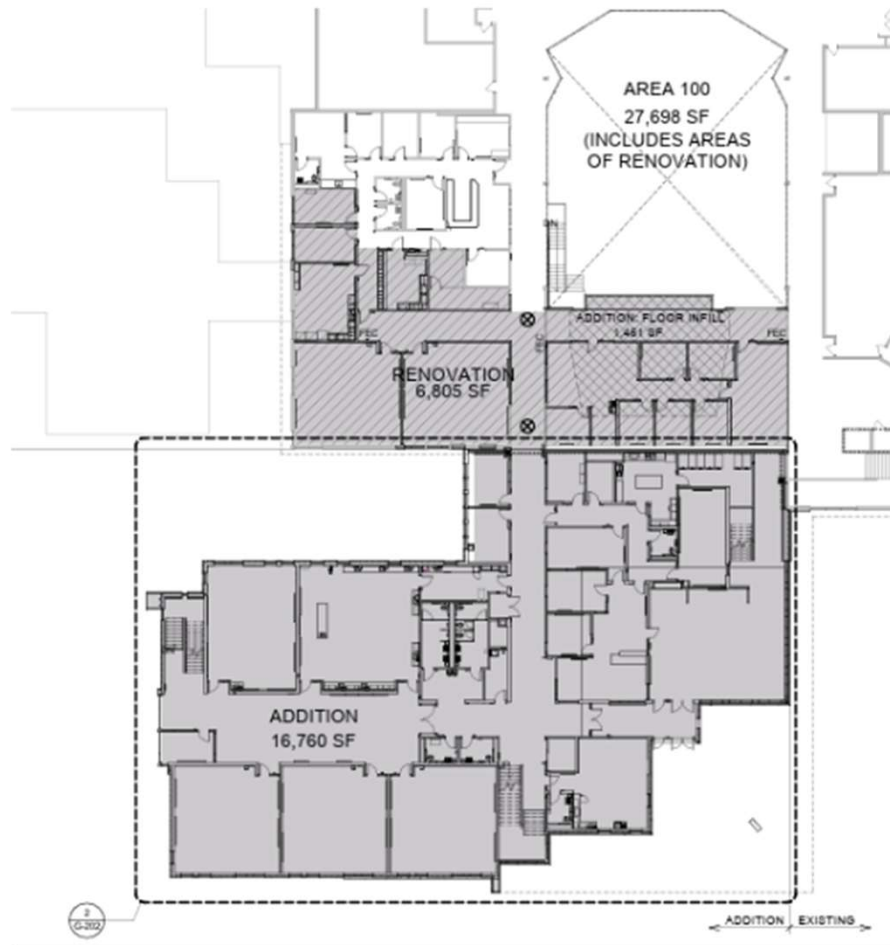

Second floor

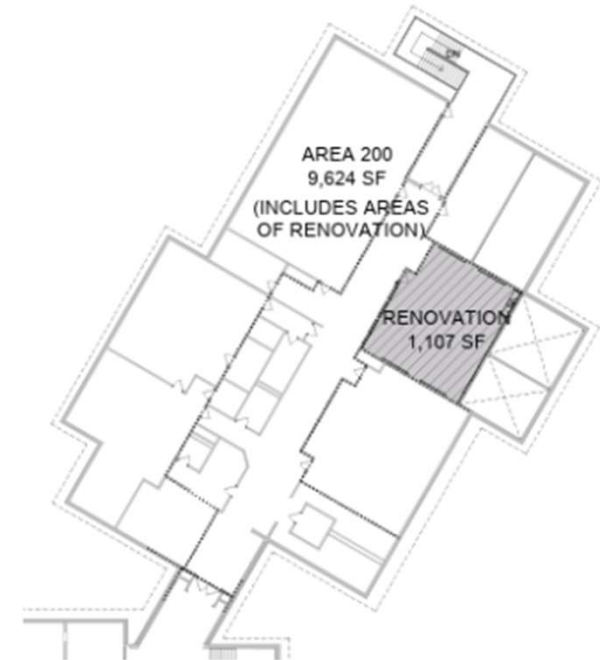

Bonney Lake HS Intersection - Project

Prime Designer: Sitts & Hill Engineer

Traffic Engineer: Transpo

Landscape Architect: Fora Landscape Architects

GC/CM Contractor: Korsmo Construction

Bonney Lake HS Intersection - Project Update

- Permit comments received and responded to
- Project schedule pushed to Summer 2027 due to permit timing

Bonney Lake HS Project- Risks & Opportunities


Risks:

- Additional permit comments adding cost
- Gas prices' effect on material and construction costs

Opportunities:

- N/A

Bonney Lake HS Intersection

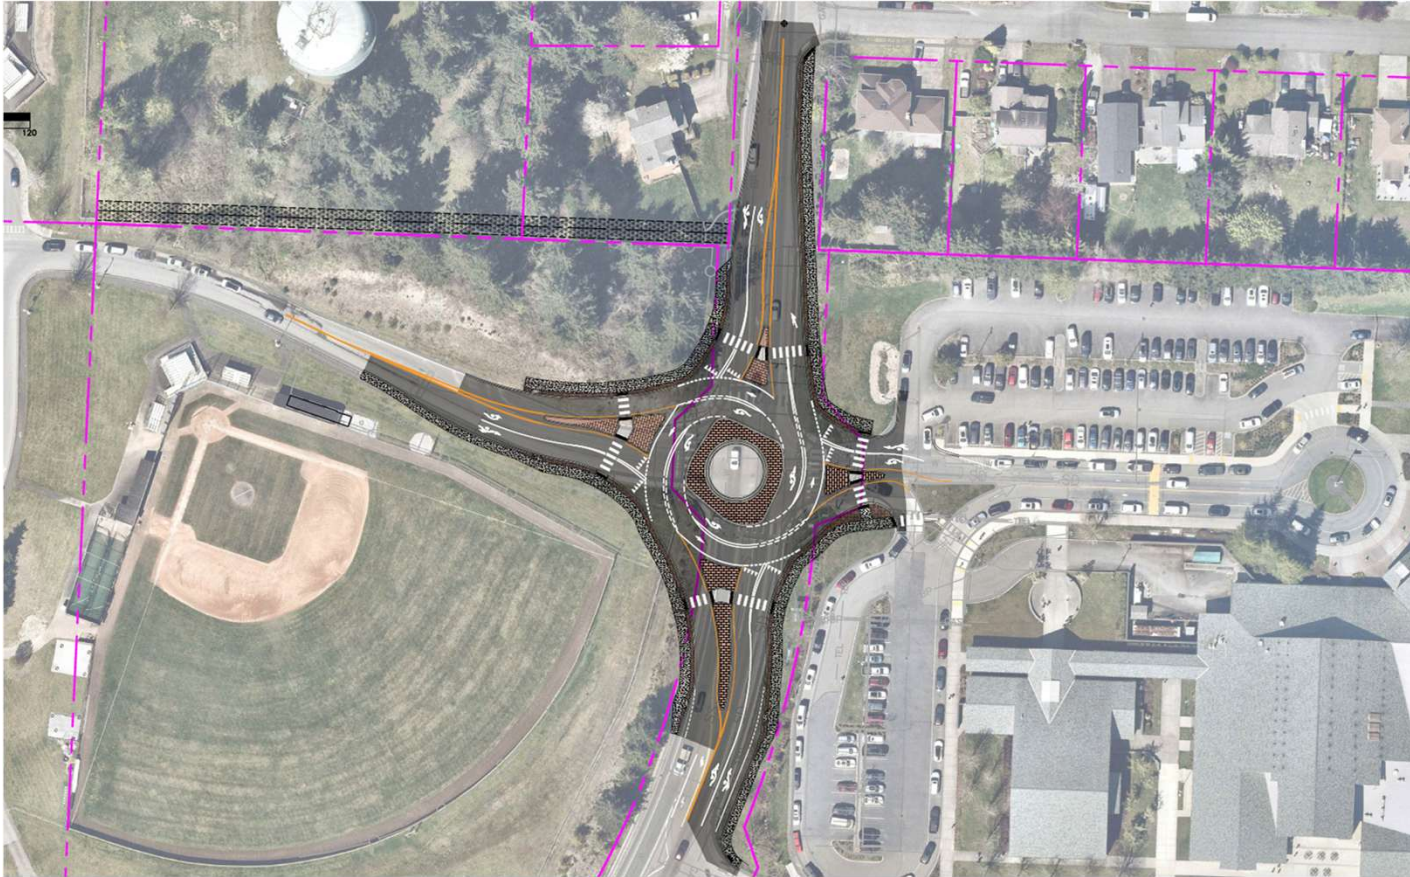

Bonney Lake HS Expansion & Intersection - Project Financials

Metric	Amount	Notes
Current project budget	\$76,882,286	Includes all approved contingencies
Spent to date	\$3,690,186	Paid through April 2026
Encumbered / committed	\$5,161,520	Contracts, purchase orders, amendments, change orders
Spent + committed	\$8,851,706	Best current measure of financial progress
Remaining budget	\$68,030,580	Current budget less spent and committed
Current construction estimate	\$54,706,976	Current estimate (Roundabout not included)
Project Contingencies	\$7,992,247	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Bonney Lake HS Expansion & Intersection - Schedule

1

BLHS Expansion	959 days	Mon 2/3/25	Wed 10/4/28	34%
EdSpec	75 days	Mon 2/3/25	Fri 5/16/25	100%
Schematic Design	79 days	Tue 5/13/25	Fri 8/29/25	100%
Design Development	90 days	Tue 10/28/25	Mon 3/2/26	100%
Contruction Drawings	79 days	Tue 3/3/26	Fri 6/19/26	95%
Permit	121 days	Mon 2/16/26	Fri 7/31/26	40%
Bid Mini-MACC	1 day	Tue 6/2/26	Tue 6/2/26	100%
Construct Mini-MACC	60 days	Mon 6/15/26	Thu 9/3/26	0%
Bid Opening	20 days	Mon 8/3/26	Fri 8/28/26	0%
Construct	523 days	Mon 8/31/26	Wed 8/30/28	0%
Occupy	25 days	Thu 8/31/28	Wed 10/4/28	0%
BLHS Intersection	776 days	Wed 2/5/25	Tue 1/25/28	42%
Develop Civil & LS Drawings	160 days	Wed 2/5/25	Tue 9/16/25	100%
Permit	150 days	Thu 3/5/26	Tue 9/29/26	75%
DELAY - Missed Season due to Permits	100 days	Wed 9/30/26	Tue 2/16/27	0%
Bid	45 days	Wed 2/17/27	Tue 4/20/27	0%
Construct	180 days	Wed 4/21/27	Tue 12/28/27	0%
City Acceptance	20 days	Wed 12/29/27	Tue 1/25/28	0%

- 1 Need a little more of the top of this schedule to see the timeline
John Boatman, 5/19/2026

Summer High School Master Plan - Project Team

Architect: Hutteball + Oremus Architecture, Inc.

GC/CM Contractor: Skanska USA Building

Structural Engineer: PCS Structural Solutions

Mechanical Engineer: Metrix Engineers

Electrical Engineer: Hargis Engineers

Civil Engineer: Jacobsen Consulting Engineers

Landscape Architect: Fora Landscape Architects

Sumner High School Master Plan- Project Update

- **Construction documents at 90% completion**
- **Permit comments received and responded to**
- **Contracted for early works (earthwork and structure)**
- **Bid opening for MACC in July**
- **PRC presentation for Phase 3 on May 28**
- **Hutteball + Oremus selected for Phase 3 Architectural Services**

Sumner High School Phase 2 - Risks & Opportunities

Risks:

- Permit status
- Construction bid environment
- Gas prices' effect on material costs


Opportunities:


- Joint outreach event held in May. Another scheduled for July.

Sumner HS Phase II



First floor

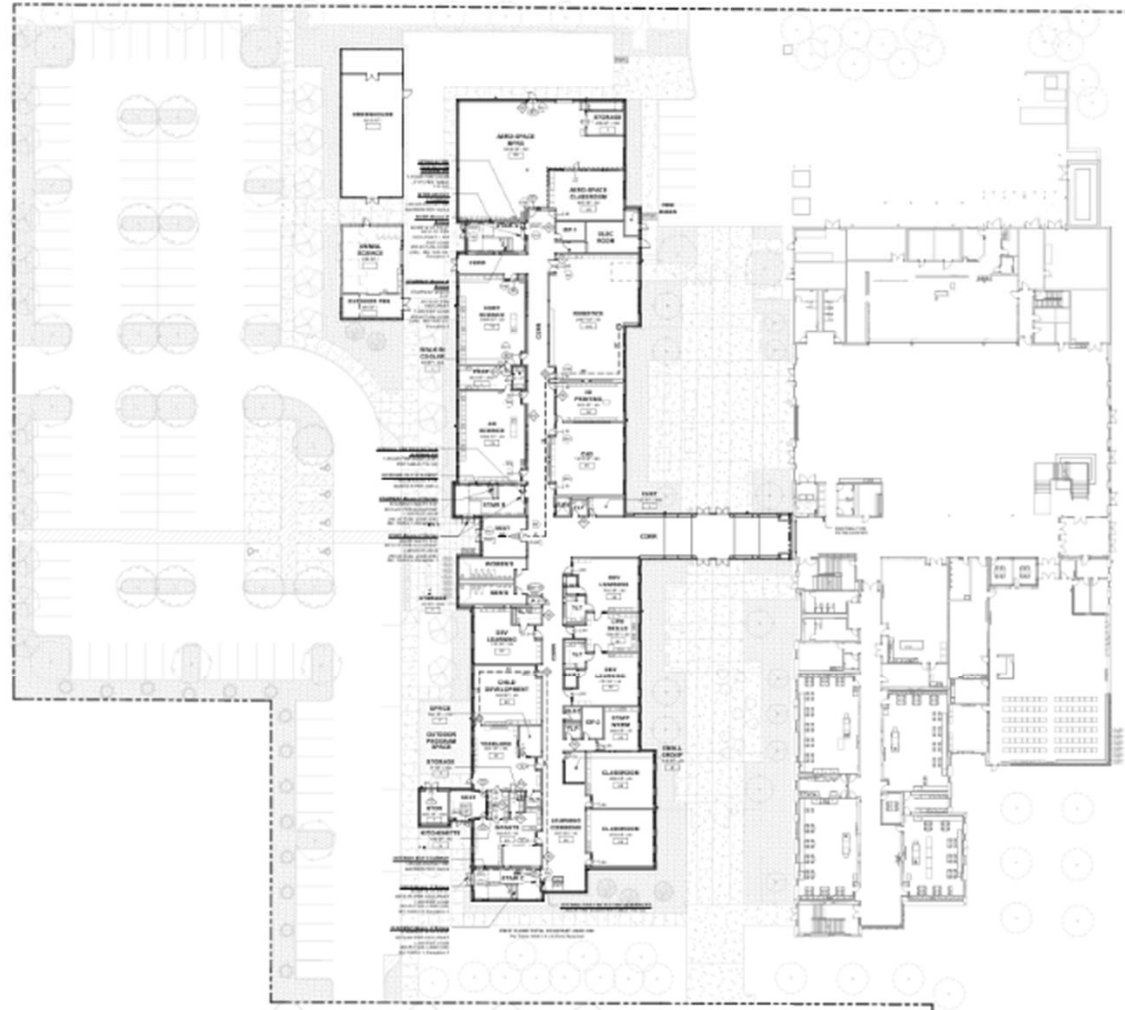


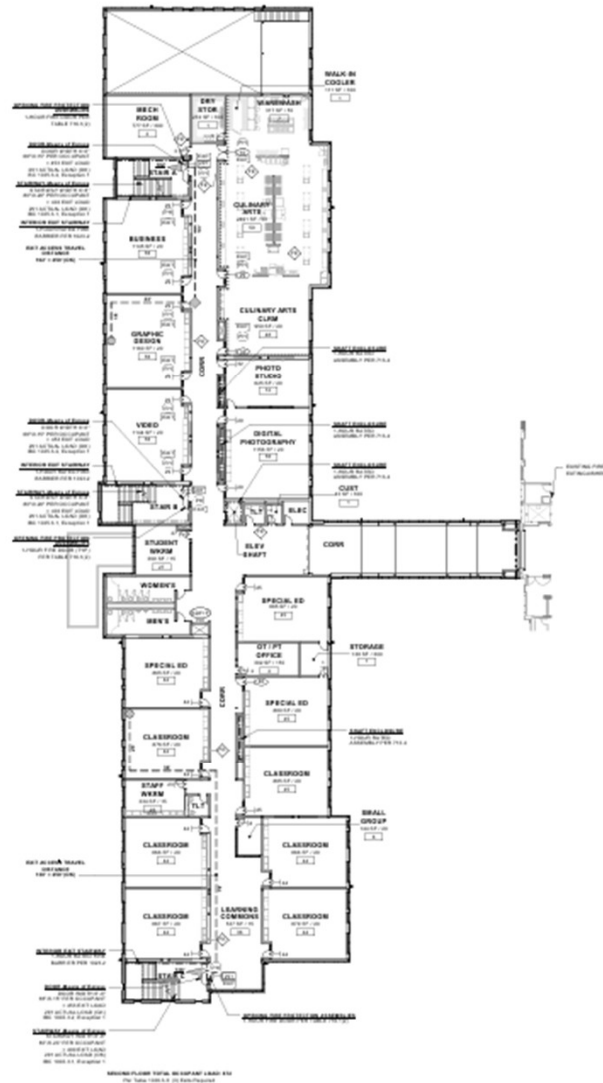

SECOND FLOOR EGRESS PLAN
SCALE: 1/8" = 1'-0"



THIRD FLOOR EGRESS PLAN
SCALE: 1/8" = 1'-0"

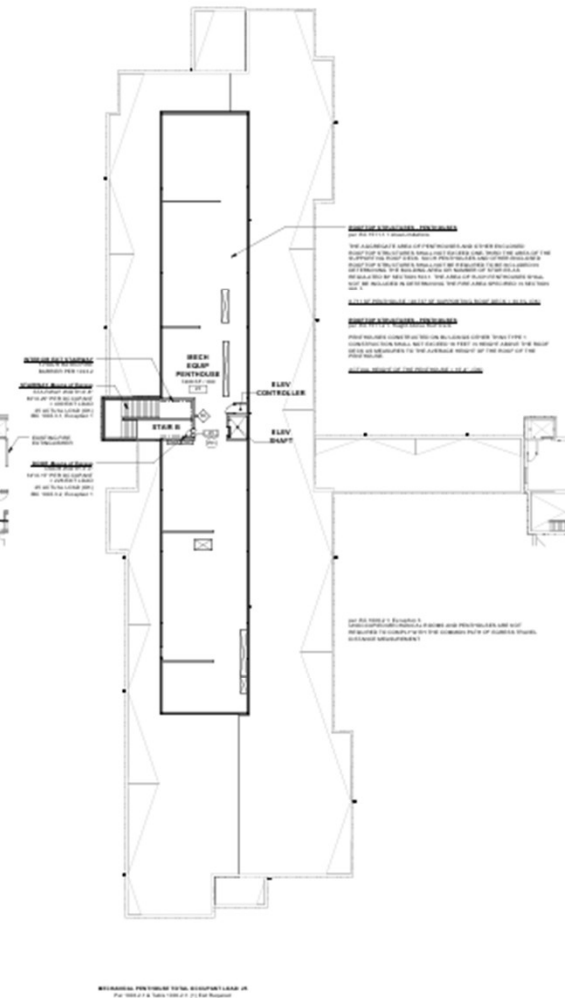

MECH EQUIP PENTHOUSE EGRESS PLAN
SCALE: 1/8" = 1'-0"

Sumner High School Master Plan – West Building Project Financials

Metric	Amount	Notes
Current project budget	\$113,540,360	Includes all approved contingencies
Spent to date	\$5,527,432	Paid through April 2026
Encumbered / committed	\$8,670,922	Contracts, purchase orders, amendments, change orders
Spent + committed	\$14,198,354	Best current measure of financial progress
Remaining budget	\$99,342,006	Current budget less spent and committed
Current construction estimate	\$83,798,702	Current estimate
Project Contingencies	\$12,947,825	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Sumner High School Master Plan – East Building Project Financials

Metric	Amount	Notes
Current project budget	\$298,239,957	Includes all approved contingencies
Spent to date	\$657	Paid through April 2026
Encumbered / committed	\$0	Contracts, purchase orders, amendments, change orders
Spent + committed	\$657	Best current measure of financial progress
Remaining budget	\$298,239,300	Current budget less spent and committed
Current construction estimate	\$232,441,078	Current estimate
Project Contingencies	\$31,000,000	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Sumner High School Master Plan - Schedule Phase 2

SHS Phase 2 - West Building	953 days	Wed 2/5/25	Thu 9/28/28	42%
EdSpec	80 days	Wed 2/5/25	Tue 5/27/25	100%
Schematic Design	50 days	Wed 4/30/25	Tue 7/8/25	100%
Design Development	65 days	Wed 7/9/25	Tue 10/7/25	100%
Construction Drawings	150 days	Wed 10/8/25	Tue 5/5/26	95%
Permit	150 days	Mon 3/2/26	Thu 9/24/26	80%
Bid Mini-MACC	1 day	Mon 5/18/26	Mon 5/18/26	100%
Construct Mini-MACC	60 days	Mon 6/15/26	Thu 9/3/26	0%
Bid Opening	1 day	Thu 7/2/26	Thu 7/2/26	0%
Construct	500 days	Fri 9/25/26	Thu 8/24/28	0%
Occupy	25 days	Fri 8/25/28	Thu 9/28/28	0%

Sumner High School Master Plan - Schedule Phase 3

SHS Phase 3	1629 days	Fri 5/1/26	Tue 7/27/32	0%
Select Design Team	0 days	Fri 5/1/26	Fri 5/1/26	100%
PRC Approval	0 days	Thu 5/28/26	Thu 5/28/26	100%
GC/CM Selection	40 days	Thu 5/28/26	Tue 7/21/26	0%
EdSpec	80 days	Wed 7/22/26	Tue 11/10/26	0%
Schematic Design	75 days	Wed 10/14/26	Tue 1/26/27	0%
Design Development	110 days	Wed 1/27/27	Tue 6/29/27	0%
Construction Drawings	150 days	Wed 6/30/27	Tue 1/25/28	0%
Permit Early Work	120 days	Tue 12/1/26	Mon 5/17/27	0%
Bid Early Work	30 days	Tue 3/9/27	Mon 4/19/27	0%
Construct Early Work	180 days	Tue 4/20/27	Mon 12/27/27	0%
Permit	150 days	Wed 6/30/27	Tue 1/25/28	0%
Bid - Middle Work	30 days	Wed 1/26/28	Tue 3/7/28	0%
Construct - Middle Work	650 days	Wed 3/8/28	Tue 9/3/30	0%
Bid - Late Work	30 days	Wed 6/12/30	Tue 7/23/30	0%
Construct - Late Work	500 days	Wed 7/24/30	Tue 6/22/32	0%
Occupy	25 days	Wed 6/23/32	Tue 7/27/32	0%

New Middle School @ Tehaleh - Project Team

Architect: McGranahanPBK

Structural Engineer: PCS Structural Solutions

Mechanical/Electrical Engineer: Hargis Engineers

Civil Engineer: Sitts & Hill Engineers

Landscape Architect: Fora Landscape Architects

New Middle School @ Tehaleh - Project Update

- Value Engineering Study complete, district evaluating options
- 100% design development drawings completed June 4th
- Road and utilities under construction by developer



New Middle School @ Tehaleh





New Middle School @ Tehaleh - Project Financials

Metric	Amount	Notes
Current project budget	\$200,000,000	Includes all approved contingencies
Spent to date	\$3,464,774	Paid through April 2026
Encumbered / committed	\$9,586,309	Contracts, purchase orders, amendments, change orders
Spent + committed	\$13,051,083	Best current measure of financial progress
Remaining budget	\$186,948,917	Current budget less spent and committed
Current construction estimate	\$136,833,751	Current estimate
Project Contingencies	\$20,280,592	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

New Middle School @ Tehaleh - Schedule

New Middle School @ Tehaleh	1115 days	Wed 2/5/25	Mon 5/14/29	28%
EdSpec	100 days	Wed 2/5/25	Tue 6/24/25	100%
Schematic Design	120 days	Wed 6/25/25	Tue 12/9/25	100%
Design Development	127 days	Wed 12/10/25	Thu 6/4/26	100%
Contruction Drawings	160 days	Fri 6/5/26	Wed 1/13/27	0%
Permit	180 days	Tue 9/1/26	Mon 5/10/27	0%
Bid	30 days	Thu 1/14/27	Wed 2/24/27	0%
Construct	500 days	Tue 5/11/27	Mon 4/9/29	0%
Occupy	25 days	Tue 4/10/29	Mon 5/14/29	0%

Daffodil Valley Elementary Field Improvements - Project Team

Landscape Architect: Second Nature Consulting

Civil Engineer: Momentum Civil

Architecture: Zervas Group

Structural Engineer: Kingworks

Mechanical/Electrical Engineer: Hultz BHU

Daffodil Valley Elementary Field Improvements - Project Update

- Received permit comments
- Developing street lighting as required by City of Sumner
- SEPA exemption submitted
- Bill Heath sale in process

Daffodil Valley Elementary Field Improvements - Risks & Opportunities

Risks:

- Permit status
- Soil/drainage mitigation and jurisdiction-required site improvements
- Long lead times and material cost escalation

Opportunities:

- Scope efficiencies may be gained by combining with Bill Heath Sports Complex improvements



Daffodil Valley Elementary Field Improvements - Project Financials

Metric	Amount	Notes
Current project budget	\$ 6,022,014	Includes all approved contingencies
Spent to date	\$352,740	Paid through [month]
Encumbered / committed	\$249,460	Contracts, purchase orders, amendments, change orders
Spent + committed	\$602,200	Best current measure of financial progress
Remaining budget	\$5,419,814	Current budget less spent and committed
Current construction estimate	\$8,604,677	Current estimate (includes alternate and sales tax)
Project Contingencies	\$881,000	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Daffodil Valley Elementary Field Improvements - Schedule

Daffodil Valley Field	655 days	Mon 6/2/25	Thu 12/2/27	33%
EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%
Schematic Design	30 days	Mon 9/29/25	Fri 11/7/25	100%
Design Development	40 days	Mon 11/10/25	Fri 1/2/26	100%
Contruction Drawings	40 days	Mon 1/5/26	Fri 2/27/26	100%
Permit	90 days	Mon 3/2/26	Thu 7/2/26	80%
DELAY-Bill Heath Purchase	240 days	Mon 6/1/26	Thu 4/29/27	0%
Bid	30 days	Fri 4/30/27	Thu 6/10/27	0%
Construct	120 days	Fri 6/11/27	Thu 11/25/27	0%
Occupy	5 days	Fri 11/26/27	Thu 12/2/27	0%

Donald Eismann Elementary Parking, Queuing and Field Improvements - Project Team

Contractor: Premier Field Development

Civil Engineer: Ethos Civil

Landscape Architect: KG Designs

Electrical Engineer: Tres West Engineers

Donald Eismann Elementary Parking, Queuing and Field Improvements - Project Update

- Field areas are currently under construction
- Parking lot work starts the day after school is out, June 18th
- Currently on schedule for completion late summer

Donald Eismann Elementary Parking, Queuing and Field Improvements



Donald Eismann Elementary Parking, Queuing and Field Improvements



Donald Eismann Elementary Parking, Queuing and Field Improvements - Project Financials

Metric	Amount	Notes
Current project budget	\$ 7,806,605	Includes all approved contingencies
Spent to date	\$307,778	Paid through April 2026
Encumbered / committed	\$4,622,504	Contracts, purchase orders, amendments, change orders
Spent + committed	\$4,931,281	Best current measure of financial progress
Remaining budget	\$2,875,324	Current budget less spent and committed
Current construction estimate	\$4,027,986	Current estimate (Storage building not included)
Project Contingencies	\$1,144,968	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Donald Eismann Elementary Parking, Queuing and Field Improvements - Schedule

Donald Eisman Queueing & Field	340 days	Mon 6/2/25	Thu 9/17/26	81%
EdSpec	20 days	Mon 6/2/25	Fri 6/27/25	100%
Schematic Design	75 days	Mon 6/30/25	Fri 10/10/25	100%
Design Development	30 days	Mon 10/13/25	Fri 11/21/25	100%
Contruction Drawings	45 days	Mon 11/24/25	Fri 1/23/26	100%
Permit	120 days	Mon 11/24/25	Fri 5/8/26	100%
Bid	30 days	Fri 2/27/26	Thu 4/9/26	100%
Construct	90 days	Mon 5/11/26	Thu 9/10/26	20%
Occupy	5 days	Fri 9/11/26	Thu 9/17/26	0%

Crestwood Elementary Improvements - Project Team

Architect: Studio Meng Strazzara

Mechanical/Electrical Engineer: Hargis

Crestwood Elementary Improvements - Project Update

- Presented room designs to staff
- Working on design for one-off spaces
- Working on estimates
- Flooring purchased for Summer 2026

Crestwood Elementary Improvements - Risks & Opportunities

Risks:

- Scope exceeds budget

Opportunities:

- Augmenting project budgets could allow us to complete additional scope needs of the building
- Exterior classroom doors


Crestwood Elementary Improvements



Crestwood Elementary Improvements



Crestwood Elementary Improvements

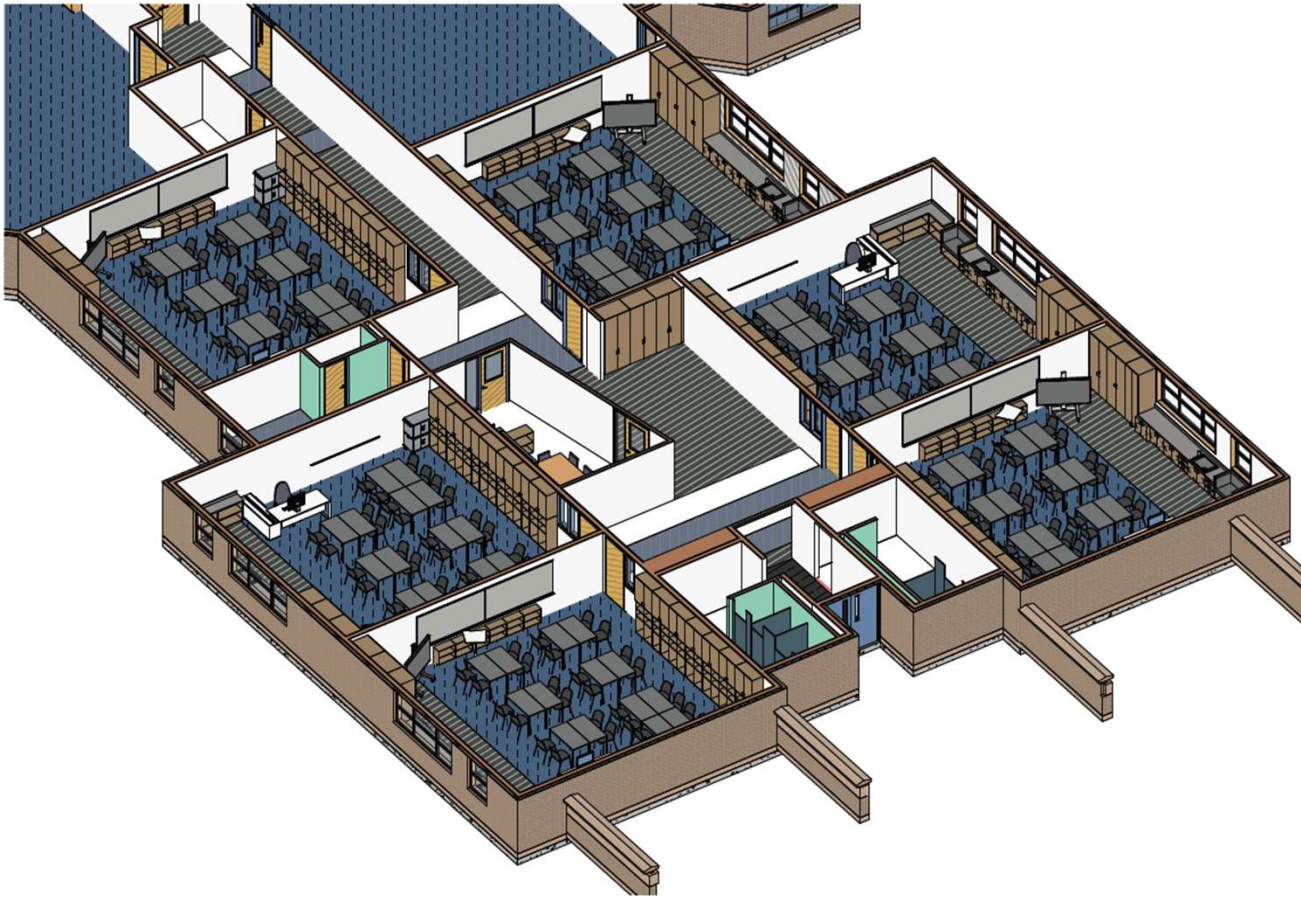

Crestwood Elementary Improvements - Project Financials

Metric	Amount	Notes
Current project budget	\$ 2,885,048	Includes all approved contingencies
Spent to date	\$90,076	Paid through April 2026
Encumbered / committed	\$608,092	Contracts, purchase orders, amendments, change orders
Spent + committed	\$698,168	Best current measure of financial progress
Remaining budget	\$2,186,880	Current budget less spent and committed
Current construction estimate	N/A	Current estimate (Scope not complete)
Project Contingencies	\$403,076	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Crestwood Elementary Improvements - Schedule

Crestwood Improvements	888 days	Fri 6/27/25	Mon 11/20/28	23%
Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25	100%
EdSpec	120 days	Fri 9/19/25	Thu 3/5/26	100%
Schematic Design	63 days	Fri 3/6/26	Tue 6/2/26	100%
Design Development	60 days	Wed 6/3/26	Mon 8/24/26	0%
Flooring Installation	60 days	Mon 6/15/26	Thu 9/3/26	0%
Contruction Drawings	90 days	Tue 8/25/26	Mon 12/28/26	0%
Permit	75 days	Tue 8/25/26	Mon 12/7/26	0%
Bid	30 days	Tue 10/27/26	Mon 12/7/26	0%
Construct	500 days	Tue 12/8/26	Mon 11/6/28	0%
Occupy	10 days	Tue 11/7/28	Mon 11/20/28	0%

Liberty Ridge Elementary Improvements - Project Team

Architect: fi Architecture

Mechanical/Electrical Engineer: TBD

Liberty Ridge Elementary Improvements - Project Update

- Presented room designs to Staff
- Working on design for one-off spaces
- Working on estimates
- Flooring purchased for Summer 2026

Liberty Ridge Elementary Improvements - Risks & Opportunities


Risks:

- Scope exceeds budget

Opportunities:

- Augmenting project budgets could allow us to complete additional scope needs of the building
- Exterior classroom doors

Liberty Ridge Elementary Improvements

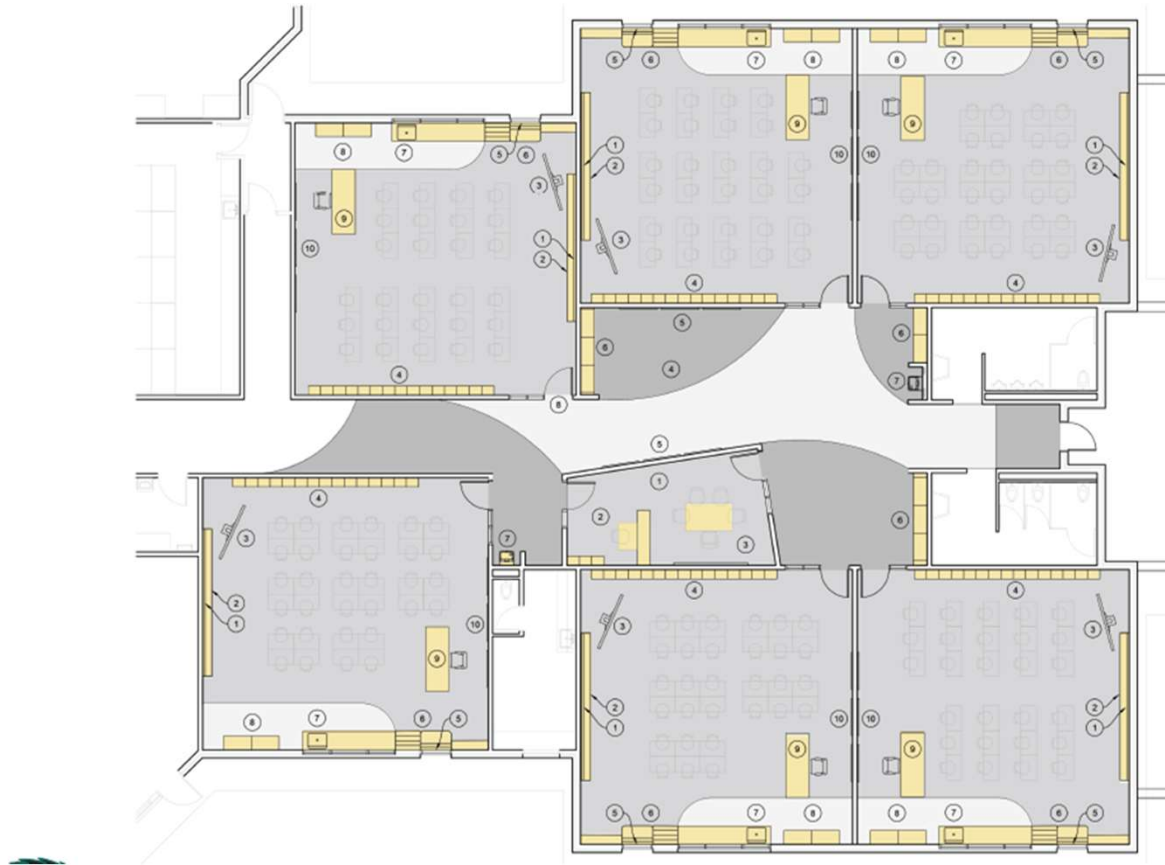

Liberty Ridge Elementary Improvements



Liberty Ridge Elementary Improvements



Liberty Ridge Elementary Improvements - Project Financials

Metric	Amount	Notes
Current project budget	\$ 2,885,048	Includes all approved contingencies
Spent to date	\$73,288	Paid through April 2026
Encumbered / committed	\$519,247	Contracts, purchase orders, amendments, change orders
Spent + committed	\$592,535	Best current measure of financial progress
Remaining budget	\$2,292,513	Current budget less spent and committed
Current construction estimate	N/A	Current estimate (Scope not complete)
Project Contingencies	\$403,076	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Liberty Ridge Elementary Improvements - Schedule

LRE Improvements	888 days	Fri 6/27/25	Mon 11/20/28	23%
Architect Selection	60 days	Fri 6/27/25	Thu 9/18/25	100%
EdSpec	120 days	Fri 9/19/25	Thu 3/5/26	100%
Schematic Design	63 days	Fri 3/6/26	Tue 6/2/26	100%
Design Development	60 days	Wed 6/3/26	Mon 8/24/26	0%
Flooring Installation	60 days	Mon 6/15/26	Thu 9/3/26	0%
Contruction Drawings	90 days	Tue 8/25/26	Mon 12/28/26	0%
Permit	75 days	Tue 8/25/26	Mon 12/7/26	0%
Bid	30 days	Tue 10/27/26	Mon 12/7/26	0%
Construct	500 days	Tue 12/8/26	Mon 11/6/28	0%
Occupy	10 days	Tue 11/7/28	Mon 11/20/28	0%

Tehaleh Heights Elementary Expansion - Project Team

Architecture: McGranahanPBK

GC/CM: Absher Construction

Mechanical/Electrical Engineer: Hargis

Structural Engineer: PCS Structural Solutions

Landscape Architect: Fora Landscape Architects

Civil Engineer: Sitts & Hill

Tehaleh Heights Elementary Expansion - Project Update

- Pre-construction contract executed
- Coordinating potholing
- Coordinating traffic with developer
- Schematic design underway
- Joint outreach event held in May. Another scheduled for July.

Tehaleh Heights Elementary Expansion



Tehaleh Heights Elementary Expansion



Tehaleh Heights Elementary Expansion - Project Financials

Metric	Amount	Notes
Current project budget	\$ 19,019,250	Includes all approved contingencies
Spent to date	\$163,698	Paid through [month]
Encumbered / committed	\$2,383,773	Contracts, purchase orders, amendments, change orders
Spent + committed	\$2,547,470	Best current measure of financial progress
Remaining budget	\$16,471,780	Current budget less spent and committed
Current construction estimate	N/A	Current estimate (Scope not complete)
Project Contingencies	\$1,572,501	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Tehaleh Heights Elementary Expansion - Schedule

Tehaleh Heights Elementary	660 days	Wed 2/4/26	Mon 8/14/28	12%
EdSpec	30 days	Wed 2/4/26	Tue 3/17/26	100%
Schematic Design	60 days	Wed 3/18/26	Tue 6/9/26	100%
Design Development	60 days	Wed 6/10/26	Mon 8/31/26	0%
Contruction Drawings	90 days	Tue 9/1/26	Mon 1/4/27	0%
Permit	120 days	Tue 9/1/26	Mon 2/15/27	0%
Bid	50 days	Tue 2/16/27	Mon 4/26/27	0%
Construct	320 days	Tue 4/27/27	Mon 7/17/28	0%
Occupy	20 days	Tue 7/18/28	Mon 8/14/28	0%

Energy Efficiency - Project Update

- LED lighting conversion begins June 16
 - Bonney Lake High School
 - Lakeridge Middle School
 - Mountain View Middle School
 - Sumner Middle School
- Eligible for PSE incentives based on project scope

Energy Efficiency - Project Financials

Metric	Amount	Notes
Current project budget	\$ 4,014,677	Includes all approved contingencies
Spent to date	\$9,517	Paid through April 2026
Encumbered / committed	\$2,138,223	Contracts, purchase orders, amendments, change orders
Spent + committed	\$2,147,741	Best current measure of financial progress
Remaining budget	\$1,866,936	Current budget less spent and committed
Current construction estimate	\$1,896,163	Current estimate (All secondary schools - doesn't include rebates)
Project Contingencies	\$281,027	Combined Construction, Support and Program Contingencies
Contingency accessed	\$0.00	Should tie to change management log

Energy Efficiency - Schedule

Summer Work	55 days	Tue 6/16/26	Mon 8/31/26	0%
Bonney Lake HS	50 days	Tue 6/16/26	Mon 8/24/26	0%
Electrical Panel Upgrade	1 wk	Mon 7/6/26	Fri 7/10/26 86,79,84	0%
Interior & Exterior	7 wks	Tue 6/16/26	Mon 8/3/26 86	0%
BLHS Gym Retrofit	1 wk	Tue 6/16/26	Mon 6/22/26 91SS	0%
Variable Driver Design Intent Verification	1 day	Tue 6/16/26	Tue 6/16/26 91SS	0%
Exterior & Commons Lighting Controls	5 days	Tue 8/4/26	Mon 8/10/26 90,91	0%
Punch, Start Up, CX, Inspections & Training	10 days	Tue 8/11/26	Mon 8/24/26 94	0%
Lakeridge MS	40 days	Tue 6/16/26	Mon 8/10/26	0%
Interior & Exterior	5 wks	Tue 6/16/26	Mon 7/20/26 86	0%
LRMS Gym Retrofit	1 wk	Tue 6/16/26	Mon 6/22/26 97SS	0%
Variable Driver Design Intent Verification	1 day	Tue 6/16/26	Tue 6/16/26 97SS	0%
Classroom Lighting Controls	5 days	Tue 7/21/26	Mon 7/27/26 97	0%
Punch, Start Up, CX, Inspections & Training	10 days	Tue 7/28/26	Mon 8/10/26 100	0%
Mountain View - MS	14 days	Tue 8/11/26	Fri 8/28/26	0%
Interior & Exterior	2 wks	Tue 8/11/26	Mon 8/24/26 94	0%
MVMS Gym Retrofit	1 wk	Tue 8/11/26	Mon 8/17/26 103SS	0%
Variable Driver Design Intent Verification	1 day	Tue 8/11/26	Tue 8/11/26 103SS	0%
Punch, Start Up, CX, Inspections & Training	4 days	Tue 8/25/26	Fri 8/28/26 103	0%
Sumner MS	25 days	Tue 7/28/26	Mon 8/31/26	0%
Interior & Exterior	3 wks	Tue 7/28/26	Mon 8/17/26 100	0%
SMS Gym Retrofit	1 wk	Tue 7/28/26	Mon 8/3/26 108SS	0%
Variable Driver Design Intent Verification	1 day	Tue 7/28/26	Tue 7/28/26 108SS	0%
Lighting Controls - Panel Replacement	5 days	Tue 8/18/26	Mon 8/24/26 108	0%
Punch, Start Up, CX, Inspections & Training	5 days	Tue 8/25/26	Mon 8/31/26 111	0%

COMMITTEE BUSINESS

COMMITTEE BUSINESS

- **BOC Meeting #6 requests**
- **Committee discussion on potential tours**

Questions / Requests from March 2026 BOC Meeting

Asked

1. Update on the permit process?
2. Pictures of construction?
3. How solid are our contracts, given the current state of the federal economy

Response

1. Updates are included in the project slides.
2. Only one project is in construction. Photos are in the slide deck and on the website.
3. Our contracts protect taxpayer dollars by shifting the financial risks of inflation and supply chain disruptions onto the construction company. Through a locked-in **Guaranteed Maximum Price**, the District is protected from paying extra for rising material costs, labor hikes, or rushed shipping. The company has a small, capped safety fund for market surprises, but if costs exceed that limit, **they must pay the difference out of their own pocket**. If global events cause project delays, they can get more time to finish, but they are strictly forbidden from charging the District for extra overhead. Finally, they are required to **order materials well in advance** to prevent delays before they even start.

BOC Meeting Outcomes

We learned about:

-

Key messages:

-

WHAT'S AHEAD

WHAT'S AHEAD

- Look for groundbreaking events at SHS in August and BLHS in September
- Look for a ribbon cutting to open the new field at DEE this fall
- Preview of Meeting #7, September 21, 2026
- Questions for BOC discussion at September meeting

WRAP UP

WRAP UP

- **Key messages**
 - **What were the key outcomes of this meeting?**
- **Evaluation**
- **Process**
 - **Content**
 - **Discussions**
- **Gratitude and adjournment**



THANK YOU
